

طلب فحص الأعمال - WORK INSPECTION REQUEST (WIR)

(Work Inspection Requests should be submitted at least 24 hours prior to inspection time)

WIR No. JSW-YC-SWRI-WIR-CI-2487

Rev. No.: 0

PROJECT - أسم المشروع	CONTRACT - العقد	OWNER - المالك	CONTRACTOR - المقاول
Jeddah Stormwater Drainage (JSWD)	Drainage Solution For Al Sawari Area& King Saud PS	Jeddah Municipality	AL-YAMAMA CO.

Consultant : WSP

Previous Activity WIR No: CI-2486

ITP Item No:

Work Description (وصف الأعمال) Backfilling of Trench From Manhole (MH05 to MH06) LINE LA01-3, ABC1,ABC2

B.O.Q: B1 (1.1.1)

Location (المكان): LA01-3

Compliance Statement: The Contractor hereby confirms that The Works offered for inspections are ready and complies with Contract documents & are internally inspected by contractor QC Engineer (in case of mandatory stop point inspection in the WIR the contractor shall not proceed without approval)

Drawing Ref. No. JSWM-ACM-AXXX-SW-DR-CE-01217

Inspection Date: 11/01/2026

Inspection Time: 10:00 Am

التخصص - DISCIPLINE

- ☐ Local Drainage ☐ Hydraulics ☐ Mechanical
- ☐ Roads ☐ Geotechnical ☐ Electrical
- ☐ Micro-Tunnelling ☒ Civil / Structural ☐ HSE
- ☐ Utilities ☐ Architectural ☐

☐ Other (specify):

Requested by:

Engr. Elhabib Musa
Contractor QC Representative
ممثل مراقبة الجودة للمقاول

Signature
التوقيع

Date
التاريخ

WSP Inspector Remarks (ملاحظات المشرف):

Approved based on FDT Results.

WSP Engineer Remarks (ملاحظات المهندس):

نتيجة الفحص - INSPECTION RESULT

The Works are: ☒ A: Approved يعتمد ☐ B: Approved with Comments - Resubmit يعتمد مع ملاحظات - يعاد تقديمه ☐ C: Not Approved - Resubmit ☐ D: Rejected مرفوض

WSP Inspector:

Name: A. Alhamani

Signature: A. Alhamani

Date: 27/4/2026

WSP Engineer:

Name: E. Alhamani

Signature: E. Alhamani

Date: 27/4/2026

Contractor:

Received: 27/4/2026

Signature: E. Alhamani

Date: 27/4/2026

Note: The Engineer's / Consultants approval shall not in any way relieve The Contractor of his obligation under the contract. The Contractor shall be solely responsible for The correctness, quality and coordination of The Works being offered for inspection as per The applicable Contract Conditions and Contract Clauses. Consultants' comments on The inspection requests shall not be construed as instruction to vary The Scope of Contractor by whatsoever means

CHECKLIST FOR BACK FILLING (ABOVE WATER TABLE)

Should be attached to Inspection Request (WIR)

WIR No.:

Rev. No.: 03 (11-12-19)

PROJECT

DIV/PACKAGE

OWNER

CONTRACTOR

Jeddah Stormwater Drainage (JSWD)

SWRI

Jeddah Municipality

AL-YAMAMAH

Pipe Diameter: _____

Drawing Ref. No.: JSW-ACM-AXXX-SW-DR-CE-01243

Exact Location: MH5-MH6
LA01-3

Type of Materials

☐ Ecavated Material

☐ Imported Material

	DESCRIPTION	STATUS	REMARKS
☐ 1	Compacted Foundation		
☐ 2	Gravel Bedding 70% Compaction & Surround, Water Compacted		
☐ 3	Above Top of Pipe 300mm Gravel if D>1000mm (min.) & 100mm if D<1000mm		
☐ 4	Backfilling 1st Layer with 95% Compaction <u>100%</u>	☒	<u>ABC</u>
☐ 5	Backfilling 2nd Layer with 95% Compaction <u>100%</u>	☒	<u>ABC</u>
☐ 5	Backfilling 3rd Layer with 95% Compaction		
☐ 6	Backfilling 4th Layer Etc. with 95% Compaction		
☐ 7	Backfilling 5th Layer Etc. with 95% Compaction		
☐ 8	Backfilling 6th Layer Etc. with 95% Compaction		
☐ 9	Backfilling 7th Layer Etc. with 95% Compaction		
☐ 10	Backfilling 8th Layer Etc. with 95% Compaction		
☐ 11	Backfilling 9th Layer Etc. with 95% Compaction		
☐ 12	Backfilling 10th Layer Etc. with 95% Compaction		
☐ 13	Backfilling Final Layer with 95% Compaction		
☐ 14	Geo Grid		
☐ 15	Others please specify _____		

Note: Permission to proceed does not constitute acceptance or approval of the work under inspection and does not relieve the contractor from full compliance with contractual obligations

Contractor Engineer:

Name: _____

Signature: _____

Date: _____

WSP Inspector:

Name: A. Alshamari

Signature: _____

Date: 27/11/20

WSP Engineer:

Name: _____

Signature: _____

Date: 27/11/20



IN-SITU (EDG) DENSITY TEST REPORT

Project :	مشروع تصريف حلول مياه الأمطار بمنطقة الصواري	Client No :	AG-J1336
Consultant :	W.S.P	Test Date :	30/10/2025
Contractor :	شركة اليمامة للمقاولات	Report Date :	30/10/2025
Location :	منطقة الصواري والملك سعود - جدة	Test Method:	ASTM D7698-11a

SOIL MODEL DETAILS

Description :	ABC 1st Layer LA 01-3 - mh -5 to mh - 6	Test Location :	
Maximum Dry Density (g/cm ³) :	2.283	Required Compaction % :	100
Optimum Moisture Content :	5.7		

NO	Layer No	Thickness (cm)	Wet Density (g/cm ³)	Dry Density (g/cm ³)	Percent Of Moisture	Percent Of Compaction	Remarks
1	ABC 1st Layer LA 01-3 - mh -5 to mh - 6	20	2.465	2.338	6.0	101.4	Pass
2	ABC 1st Layer LA 01-3 - mh -5 to mh - 6	20	2.534	2.351	6.1	103.1	Pass
3	ABC 1st Layer LA 01-3 - mh -5 to mh - 6	20	2.486	2.234	6.1	100.9	Pass
4	ABC 1st Layer LA 01-3 - mh -5 to mh - 6	20	2.451	2.333	6.3	102.5	Pass
5							
6							
7							
8							
9							
10							

Note

Tested By:

Mahmoud Adel

Revised By:

Mohamed Essam





IN-SITU (EDG) DENSITY TEST REPORT

Project :	مشروع تصريف حلول مياه الأمطار بمنطقة الصواري	Client No :	AG-J1336
Consultant :	W.S.P	Test Date :	01/11/2025
Contractor :	شركة اليمامة للمقاولات	Report Date :	01/11/2025
Location :	منطقه الصواري والملك سعود - جدة	Test Method:	ASTM D7698-11a

SOIL MODEL DETAILS

Description :	ABC 2nd Layer LA 01-3 - mh -5 to mh - 6	Test Location :	
Maximum Dry Density (g/cm ³) :	2.283	Required Compaction % :	100
Optimum Moisture Content :	5.7		

NO	Layer No	Thickness (cm)	Wet Density (g/cm ³)	Dry Density (g/cm ³)	Percent Of Moisture	Percent Of Compaction	Remarks
1	ABC 2nd Layer LA 01-3 - mh -5 to mh - 6	20	2.469	2.331	5.9	102.1	Pass
2	ABC 2nd Layer LA 01-3 - mh -5 to mh - 6	20	2.520	2.382	5.8	104.3	Pass
3	ABC 2nd Layer LA 01-3 - mh -5 to mh - 6	20	2.431	2.299	5.7	100.7	Pass
4	ABC 2nd Layer LA 01-3 - mh -5 to mh - 6	20	2.466	2.324	6.1	101.8	Pass
5	ABC 2nd Layer LA 01-3 - mh -5 to mh - 6	20	2.475	2.326	6.4	101.9	Pass
6							
7							
8							
9							
10							

Note

Tested By:

Mahmoud Adel

Revised By:

Mohamed Essam



**Saden Specialized Company
For Geological Consulting**

Soil Probing - Hydrological Studies - Laboratories (Concrete - Asphalt - Calibration)



**شركة سادن المتخصصة
للإستشارات الجيولوجية**

حسابات تربة - دراسات هيدرولوجية - مخبرات (خرسانة - أسفلت - معايرة)

IN-SITU (EDG) DENSITY TEST REPORT

Project :	مشروع تصريف حلول مياه الأمطار بمنطقة الصواري	Client No :	AG-J1336
Consultant :	W.S.P	Test Date :	25/08/2025
Contractor :	شركة اليمامة للمقاولات	Report Date :	25/08/2025
Location :	منطقة الصواري والملك سعود - جدة	Test Method:	ASTM D7698-11a

SOIL MODEL DETAILS

Description :	ABC Layer	Test Location :	LA01-3
Maximum Dry Density (g/cm ³) :	2.283	Required Compaction % :	100
Optimum Moisture Content :	5.7		

NO	Layer No	Thickness (cm)	Wet Density (g/cm ³)	Dry Density (g/cm ³)	Percent Of Moisture	Percent Of Compaction	Remarks
1	ABC-2nd layer -LA01-3 MH-05 to MH-06	20	2.458	2.315	6.2	101.4	Pass
2	ABC-2nd layer -LA01-3 MH-05 to MH-06	20	2.482	2.331	6.5	102.1	Pass
3	ABC-2nd layer -LA01-3 MH-05 to MH-06	20	2.459	2.317	6.1	101.5	Pass
4	ABC-2nd layer -LA01-3 MH-05 to MH-06	20	2.500	2.356	6.1	103.2	Pass
5							
6							
7							
8							
9							
10							

Note :

Tested By:

Mahmoud Adol

Revised By:

Mohamed Essam

Approved By:

Anmed Elmaghrabi

سادن المتخصصة للإستشارات الجيولوجية
SADEN SPECIALIZED CO. FOR GEOLOGICAL CONSULTING


شركة
شركة سادن المتخصصة
للإستشارات الجيولوجية

jd@saden.sa


0551706008

0122003000

رقم ج.د. ٤١٠٣٠٤٢٢٠٤٣ - شارع الملك فهد - حي النور - جدة


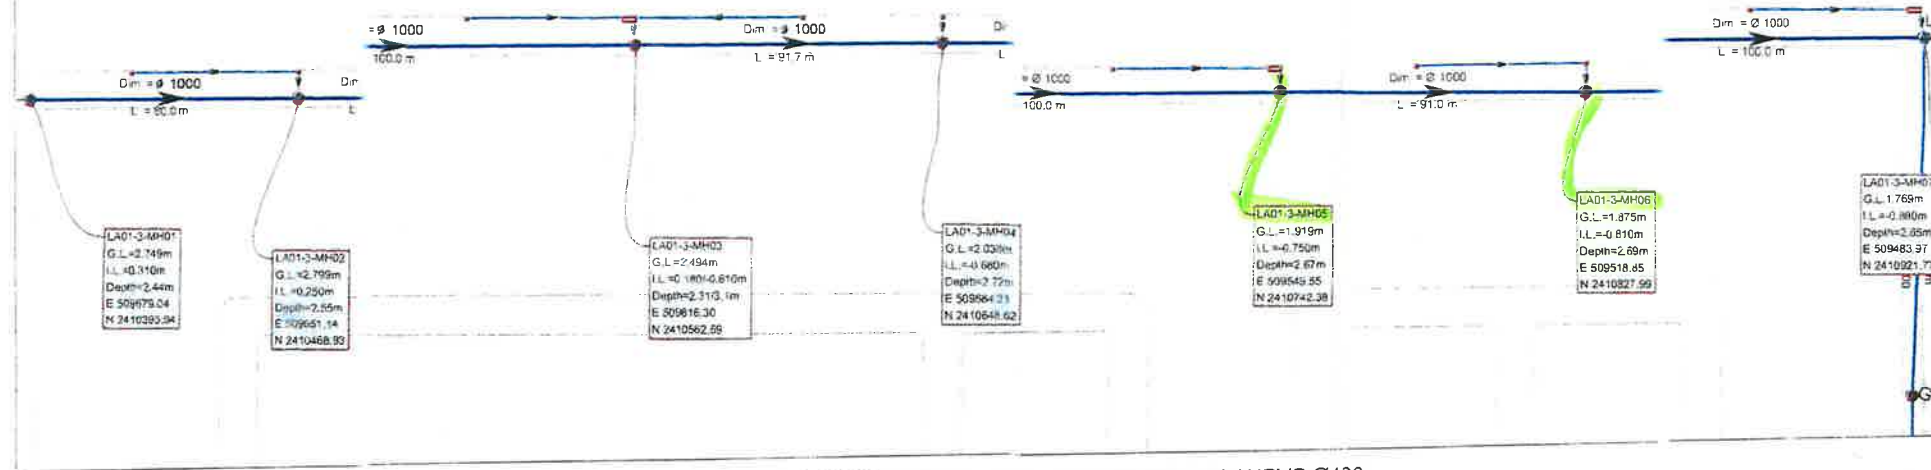


PLAN OF LINE LINE LA01-3 / RC Ø1000 / UPVC Ø400
FROM LA01-3-MH01 TO LA01-3-MH07

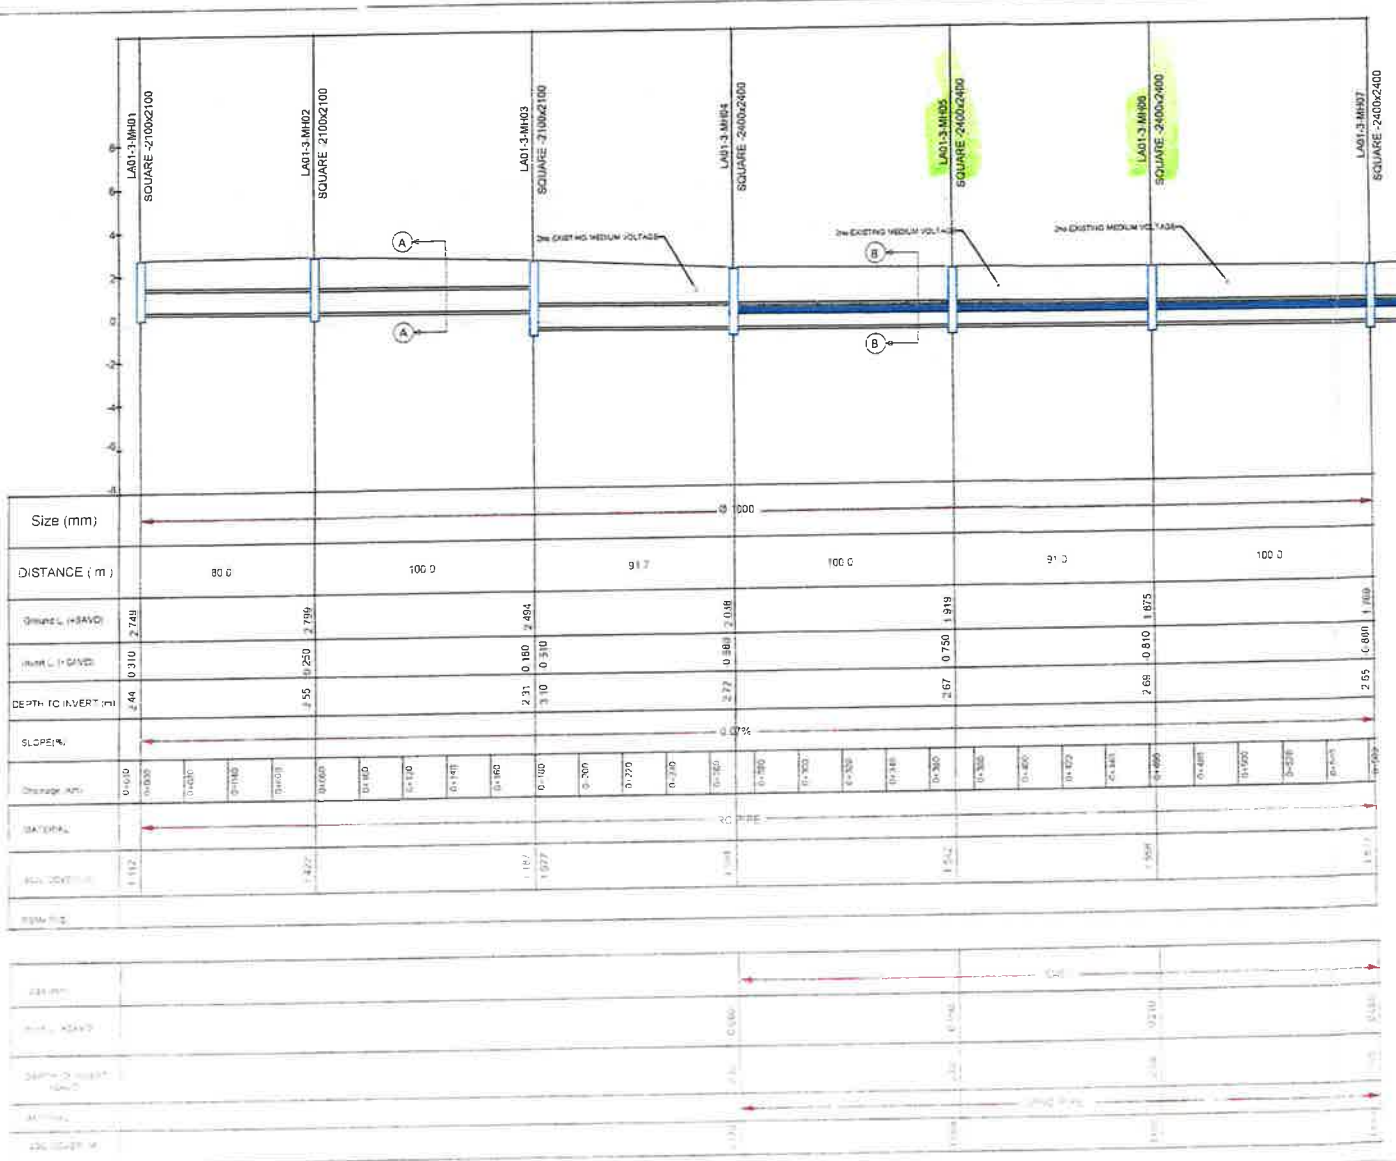


UPVC / RC PIPE PROFILE OF LINE LA01-3 / RC Ø1000 / UPVC Ø400
FROM LA01-3-MH01 TO LA01-3-MH07

CONTINUATION - REFER TO - JSW-YC-SWRI-SW-DR-CE-01218

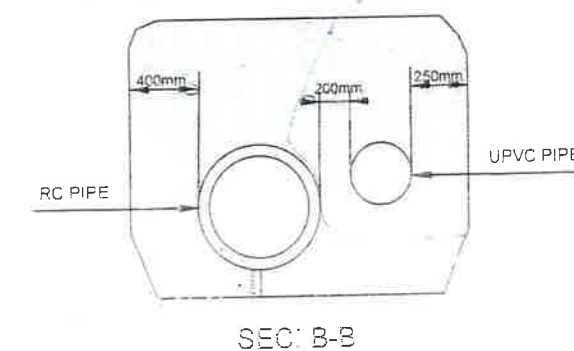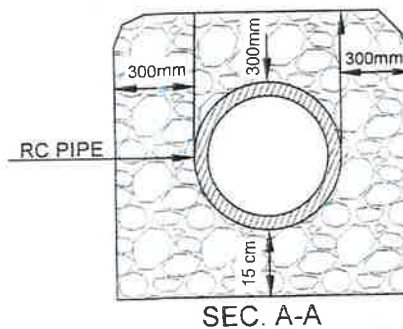

CONTINUATION - REFER TO - JSW-YC-SWRI-SW-DR-CE-01218

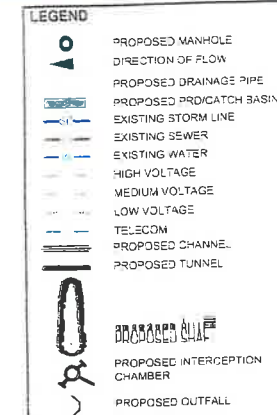

- NOTES**
- THE CONTRACTOR SHOULD VERIFY GROUND LEVELS AND SUBMIT DETAILED SHOP DRAWINGS BASED ON ACTUAL SITE SURVEY BEFORE STARTING EXCAVATION FOR PIPE LAYING.
 - CONTRACTOR MUST CONFIRM EXISTING UTILITIES TYPE, SIZE, LOCATION AND DEPTH ALONG PIPELINE ROUTE PRIOR TO COMMENCING WORKS. SOME UTILITIES SUCH AS STC AND MOBIILITY ARE OMITTED FOR CLARITY. REFER TO DRAWINGS JSW-ACM-XXX-UT-DR-CE-01201 - 01233.
 - STAKEHOLDERS MUST BE CONSULTED WITH REGARDS TO THE PIPELINE ROUTE THE EXECUTION.
 - A GEOPHYSICAL SURVEY SHOULD BE CARRIED OUT PRIOR TO WORKS COMMENCING.
 - PIPES WITH INSUFFICIENT COVER TO BE CONCRETE ENCASED. REFER TO STANDARD DETAILS.
 - RELOCATE UTILITY BASED ON SITE CONDITIONS.



- NOTES**
- FOR ABBREVIATIONS AND LEGEND REFER TO DRAWING NO. JSW-ACM-XXX-XX-DR-ZZ-00203.
 - FOR GENERAL NOTES REFER TO DRAWING NO. JSW-ACM-XXX-XX-DR-ZZ-00204.
 - LOCATIONS OF PROPOSED DRAINAGE BASINS ARE INDICATIVE ONLY. CONTRACTOR SHALL DETERMINE AND VERIFY THE SETTINGS TO ENSURE CORRECT INSTALLATION AT LOW POINTS.
 - FOR MANHOLE/PRO'S & CATCH BASINS DETAIL REFER TO STANDARD DRAWINGS.
 - FOR MANHOLE/PRO'S SCHEDULE REFER TO DRAWING NO. JSW-ACM-XXX-SW-DR-CE-06201 TO CE-06205.
 - THE CONTRACTOR SHOULD VERIFY/PROVIDE ALL REQUIRED EXISTING UTILITIES INVERT LEVELS DATA BEFORE THE EXECUTION.
 - THE UTILITIES SHOWN ARE BASED ON INFORMATION OBTAINED FROM AMANAH GIS UTILITY DATABASE DESCRIBED IN THE SCOPE OF WORKS DOCUMENTS. IT IS THE CONTRACTOR'S RESPONSIBILITY TO PROVE THE UTILITIES BEFORE STARTING THE WORK AND REPORT ANY DISCREPANCIES.

NO.	DRAWING NO.	DRAWING TITLE
1	JSW-ACM-XXX-SW-DR-CE-01217	PLAN & PROFILE - LINE LA01-3 SHEET 1 OF 1
2		
3		

ISSUE / REVISION	DESCRIPTION	APPROVED BY
02	01/08/2025	
01	22/06/2025	
00	06/10/2024	

PS Sand King & Area Sawari Al For Solution

OWNER: KINGDOM OF SAUDI ARABIA

امانة جدة

MANAGEMENT:

DESIGNER:

CONSULTANT:

DATE

SIGNATURE

APPROVAL CODE

DESCRIPTION

SIGNATURE

APPROVED

APPROVED WITH COMMENTS

RE-SUBMIT

NOT APPROVED - RESUBMIT

REJECTED

CONTRACTOR

DRAWING TITLE

AL SAWARI AREA

PLAN & PROFILE - LINE LA01-3

FROM MH01 TO MH07

SHEET 1 OF 1

PROJECT NUMBER

241-513-14-11-2

CHECKED BY

DESIGNED BY

DRAWN BY

SCALE

NTS

SHEET NO.

01 OF 03

* Ensure that the path is not clashing with existing utilities & private properties.
* Submit the related RFI for finish asphalt level (coordinating with Road department (superior) needs for PRDs, RSDs, Manholes covers)
* Use both deactivating & sharing system properly this frame is collapsible soil (sandiness)
* Coordinate with related stakeholders & suppliers providers before starting works
* The sub station should be approved before starting works
* Verify if the first quantity is enough

WE CERTIFY THAT THE SUBMITTAL HAS BEEN REVIEWED & CHECKED AND APPROVED FOR COMPLIANCE WITH THE CONTRACT DOCUMENTS

CONTRACTOR SIGNATURE
