

طلب فحص الأعمال - (WIR) WORK INSPECTION REQUEST

(Work Inspection Requests should be submitted at least 24 hours prior to inspection time)

WIR No. JSW-YC-SWRI-WIR-SU-0752

Rev. No.: 0

PROJECT - اسم المشروع	CONTRACT - العقد	OWNER - المالك	CONTRACTOR - المقاول
Jeddah Stormwater Drainage (JSWD)	Drainage Solution For Al Sawari Area & King Saud PS	Jeddah Municipality	AL-YAMAMA CO.

Consultant : WSP

Previous Activity WIR No:

ITP Item No:

Work Description (وصف الأعمال): Installation of Pipeline from Manhole (MH05 - MH06), Line (LA01-3), Dia - 400mm, UPVC Pipe From Station (0 TO 90.37)

B.O.Q: B2 (2.1.1)

Location (المكان): LA01-3

Compliance Statement: The Contractor hereby confirms that The Works offered for inspections are ready and complies with Contract documents & are internally inspected by contractor QC Engineer (in case of mandatory stop point inspection in the ITP, the contractor shall not proceed without approval)

Drawing Ref. No. JSWM-ACM-AXXX-SW-DR-CE-01217

Inspection Date: 17/05/2025

Inspection Time: 9:00 am

DISCIPLINE - التخصص

- ☐ Local Drainage ☐ Hydraulics
☐ Roads ☐ Geotechnical
☐ Micro-Tunnelling ☒ Civil / Structural
☐ Utilities ☐ Architectural

- ☐ Mechanical
☐ Electrical
☐ HSE

☐ Other (specify):

Requested by:

Engr. Elhabib Musa

Contractor QC Representative

ممثل مراقبة الجودة للمقاول

Signature

التوقيع

WSPME
SWRI

17 JUN 2025

17/5/2025

RECEIVED

Date

التاريخ

WSP Inspector Remarks (ملاحظات المشرف):

checked

WSP Engineer Remarks (ملاحظات المهندس):

INSPECTION RESULT - نتيجة الفحص

The Works are: ☒ A: Approved ☐ B: Approved with Comments - Resubmit ☐ C: Not Approved - Resubmit ☐ D: Rejected مرفوض

WSP Inspector:

Name: *Elham Abdel*

Signature: *Elham Abdel*

Date: 24/06/2025

WSP Engineer:

Name: *Raghib Heberish*

Signature: *Raghib Heberish*

Date: 25.06.2025

Note: The Engineer's / Consultants approval shall not in any way relieve The Contractor of his obligation under The Contract. The Contractor shall be solely responsible for The correctness, quality and coordination of The Works being offered for inspection as per The applicable Contract Conditions and Contract Clauses. Consultants' comments on The inspection requests shall not be construed as instruction to vary The scope of Contractor by whatsoever means

KINGDOM OF SAUDI ARABIA
MUNICIPALITY
WATER AND MASTER PLAN

JEDDAH
JEDDAH STORM



CONTRACTOR



CONSULTANT



SHEET FOR EARTH EXCAVATION DETAILS AND TOP OF PIPE

NAME OF STREET:						Existing Asphalt = 0.12m	W. Asph. =	2.504	MH SIZE		MH05(2400*2400)	MH 06(2400*2400)
LINE NO:	LA01-3	SHEET NO.:				Existing ABC = 0.30M			MH WALL THICKNESS		350mm	350mm
SLOPE:	0.070%	FROM STA:				TO STA:		FROM:MH TO:MH	MH05:	MH06	MH BASE THICKNESS	
WIDTH:	2.504	DIAMETER & KIND OF PIPE:				400mm UPVC		LENGTH :C.C	90.37		MH BASE LEVEL	
THICKNESS:	0.02	BEDDING:		0.15		NET LENGTH:		87.27		Depth to MH BASE		
M.H. NO.	S.T	DISTANCE	GROUND LEVEL	TYPE OF LINE RCBUPVC	INVERT LEVEL	EXCAVATION LEVEL	TOP OF PIPE LEVEL	ACTUAL TOP OF PIPE	ACTUAL EXCAVATION LEVEL	DIFFERENCE	rock. L	REMARKS
MH05	0	0.000	1.919	Parallel	-0.150							509548.058
-	1.20	1.200	1.919	Parallel	-0.151		0.229					2410744.114
-	1.55	0.350	1.919	Parallel	-0.151		0.229					
sp	2.55	1.000	1.919	Parallel	-0.152		0.228					
sp	3.30	0.750	1.919	Parallel	-0.152		0.228					
1	9.05	5.750	1.919	Parallel	-0.156		0.224					
2	14.80	5.750	1.919	Parallel	-0.160		0.220					
3	20.55	5.750	1.919	Parallel	-0.164		0.216					
4	26.30	5.750	1.919	Parallel	-0.168		0.212					
5	32.05	5.750	1.919	Parallel	-0.171		0.209					
6	37.80	5.750	1.919	Parallel	-0.175		0.205					
7	43.55	5.750	1.919	Parallel	-0.179		0.201					
8	49.30	5.750	1.919	Parallel	-0.183		0.197					
9	55.05	5.750	1.919	Parallel	-0.187		0.193					
10	60.80	5.750	1.919	Parallel	-0.191		0.189					
11	66.55	5.750	1.919	Parallel	-0.195		0.185					
12	72.30	5.750	1.919	Parallel	-0.198		0.182					
13	78.05	5.750	1.900	Parallel	-0.202		0.178					
14	83.80	5.750	1.900	Parallel	-0.206		0.174					
C.P	87.32	3.520	1.900	Parallel	-0.209		0.171					
sp	88.07	0.750	1.920	Parallel	-0.209		0.171					
sp	88.82	0.750	1.900	Parallel	-0.210		0.170					
-	89.17	0.350	1.875	Parallel	-0.210		0.170					509517.384
MH06	90.37	1.200	1.875	Parallel	-0.211							2410829.119

SURVEYOR



PROJECT MANAGER



CONSULTANT

SURVEYOR

RESIDENT ENGINEER




DRAWN BY	CHECKED BY:	CHECKED
	ARC4	CIVIL/ ST
SUBMITTAL NO.: 15W-10-SW-11-SUB-DI-05A		
DRAWING NUMBER 15W-10-SW-11-SUB-DI-05A		
SCALE:	NTS	

SFC R-R

UPVC / RC PIPE PROFILE OF LINE LA01-3 / RC Ø1000 / UPVC Ø400
FROM LA01-3-MH01 TO LA01-3-MH06

CONTRACTOR SIGNATURE

PROJECT NUMBER	003 / 7513 / 00 / 0014		
DRAWN BY	CHECKED BY:	CHECKED BY:	CHECKED BY:
	ARC4	CIVIL / STRC.	ELEC. MECH.
SUBMITTAL NO : ISN-YC-SWIR-SW-01-05406			
DRAWING NUMBER : ISN-YC-SWIR-SW-01-05407			REV NO : 00
SCALE:	NTS	SHEET NO :	01 OF 03

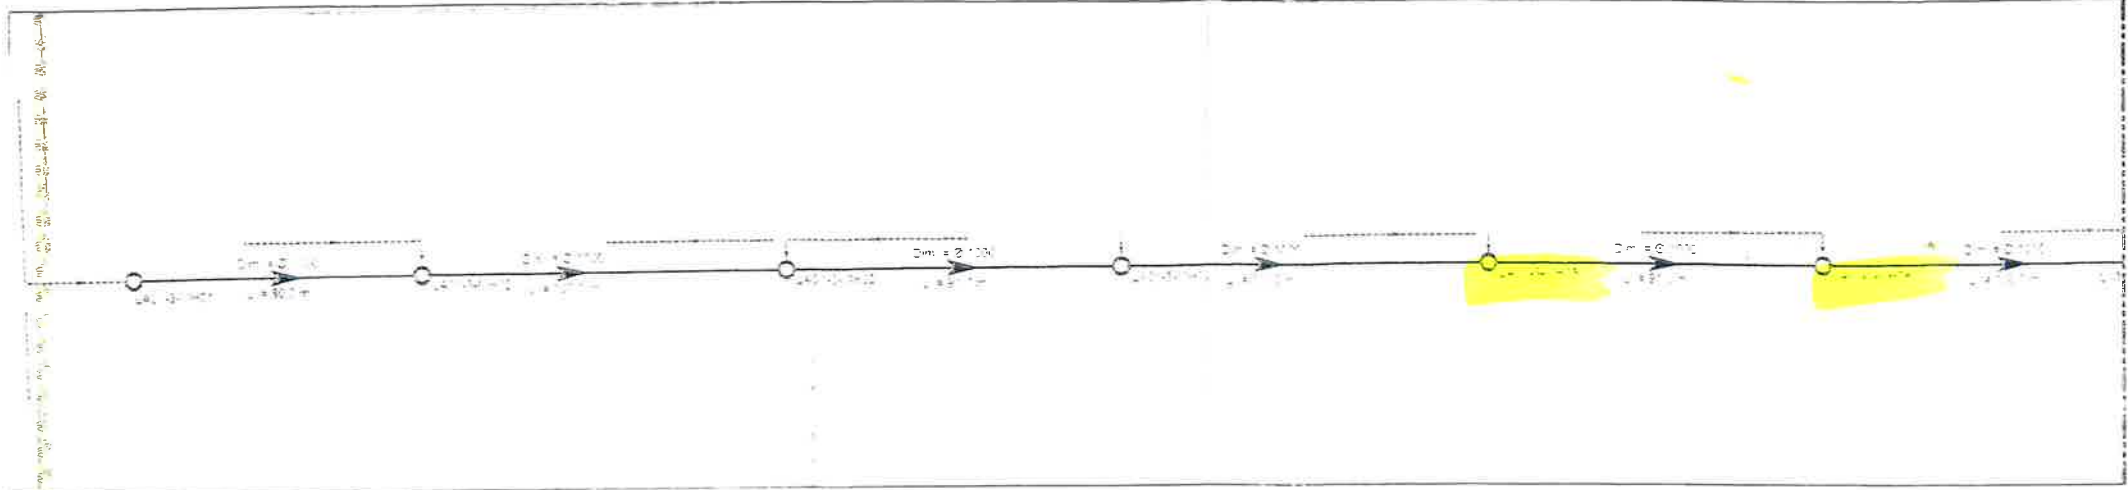

PLAN L01-3

SCALE: 1:1000




LEGEND

- PROPOSED MAN-HOLE
- PROPOSED JUNCTION BOX
- DIRECTION OF FLOW
- PROPOSED PROTECTION BASIN
- PROPOSED SW KERB INLET
- PROPOSED PROTECTION BASIN PIPE
- PROPOSED SW DRAINAGE PIPE
- PROPOSED SW DRAINAGE CULVERT
- SD EXISTING STORM LINE
- SS EXISTING SEWER
- W EXISTING WATER
- HV HIGH VOLTAGE
- MV MEDIUM VOLTAGE
- LV LOW VOLTAGE
- CB COASTAL BOUNDARY
- PROPOSED STORMWATER PIPELINE SYSTEM (BY OTHERS)


NOTES

1. FOR ABBREVIATIONS AND LEGEND REFER TO DRAWING NO. JSWM-ACM-XXXX-SW-DR-CE-01211
2. FOR GENERAL NOTES REFER TO DRAWING NO. JSWM-ACM-XXXX-SW-DR-CE-01212
3. LOCATIONS OF PROPOSED PROTECTION BASINS ARE INDICATIVE ONLY. CONTRACTOR SHALL DETERMINE AND VERIFY THE SETTINGS TO ENSURE CORRECT INSTALLATION AT LOW POINTS.
4. FOR MANHOLE/PRODS & CATCH BASINS DETAIL REFER TO STANDARD DRAWINGS.
5. FOR MANHOLE/PRODS SCHEDULE REFER TO DRAWING NO. JSWM-ACM-XXXX-SW-DR-CE-06201 TO CE-06205.
6. THE CONTRACTOR SHOULD VERIFY/PROVIDE ALL REQUIRED EXISTING UTILITIES INVERT LEVELS/DATA BEFORE THE EXECUTION.
7. THE UTILITIES SHOWN ARE BASED ON INFORMATION OBTAINED FROM AMANAH GIS UTILITY DATABASE DESCRIBED IN THE SCOPE OF WORKS DOCUMENTS. IT IS THE CONTRACTOR'S RESPONSIBILITY TO PROVE THE UTILITIES BEFORE STARTING THE WORK AND REPORT ANY DISCREPANCIES.
8. THE CONTRACTOR SHOULD VERIFY GROUND LEVELS AND SUBMIT DETAILED SHOP DRAWINGS BASED ON ACTUAL SITE SURVEY BEFORE STARTING EXCAVATION FOR PIPE LAYING.

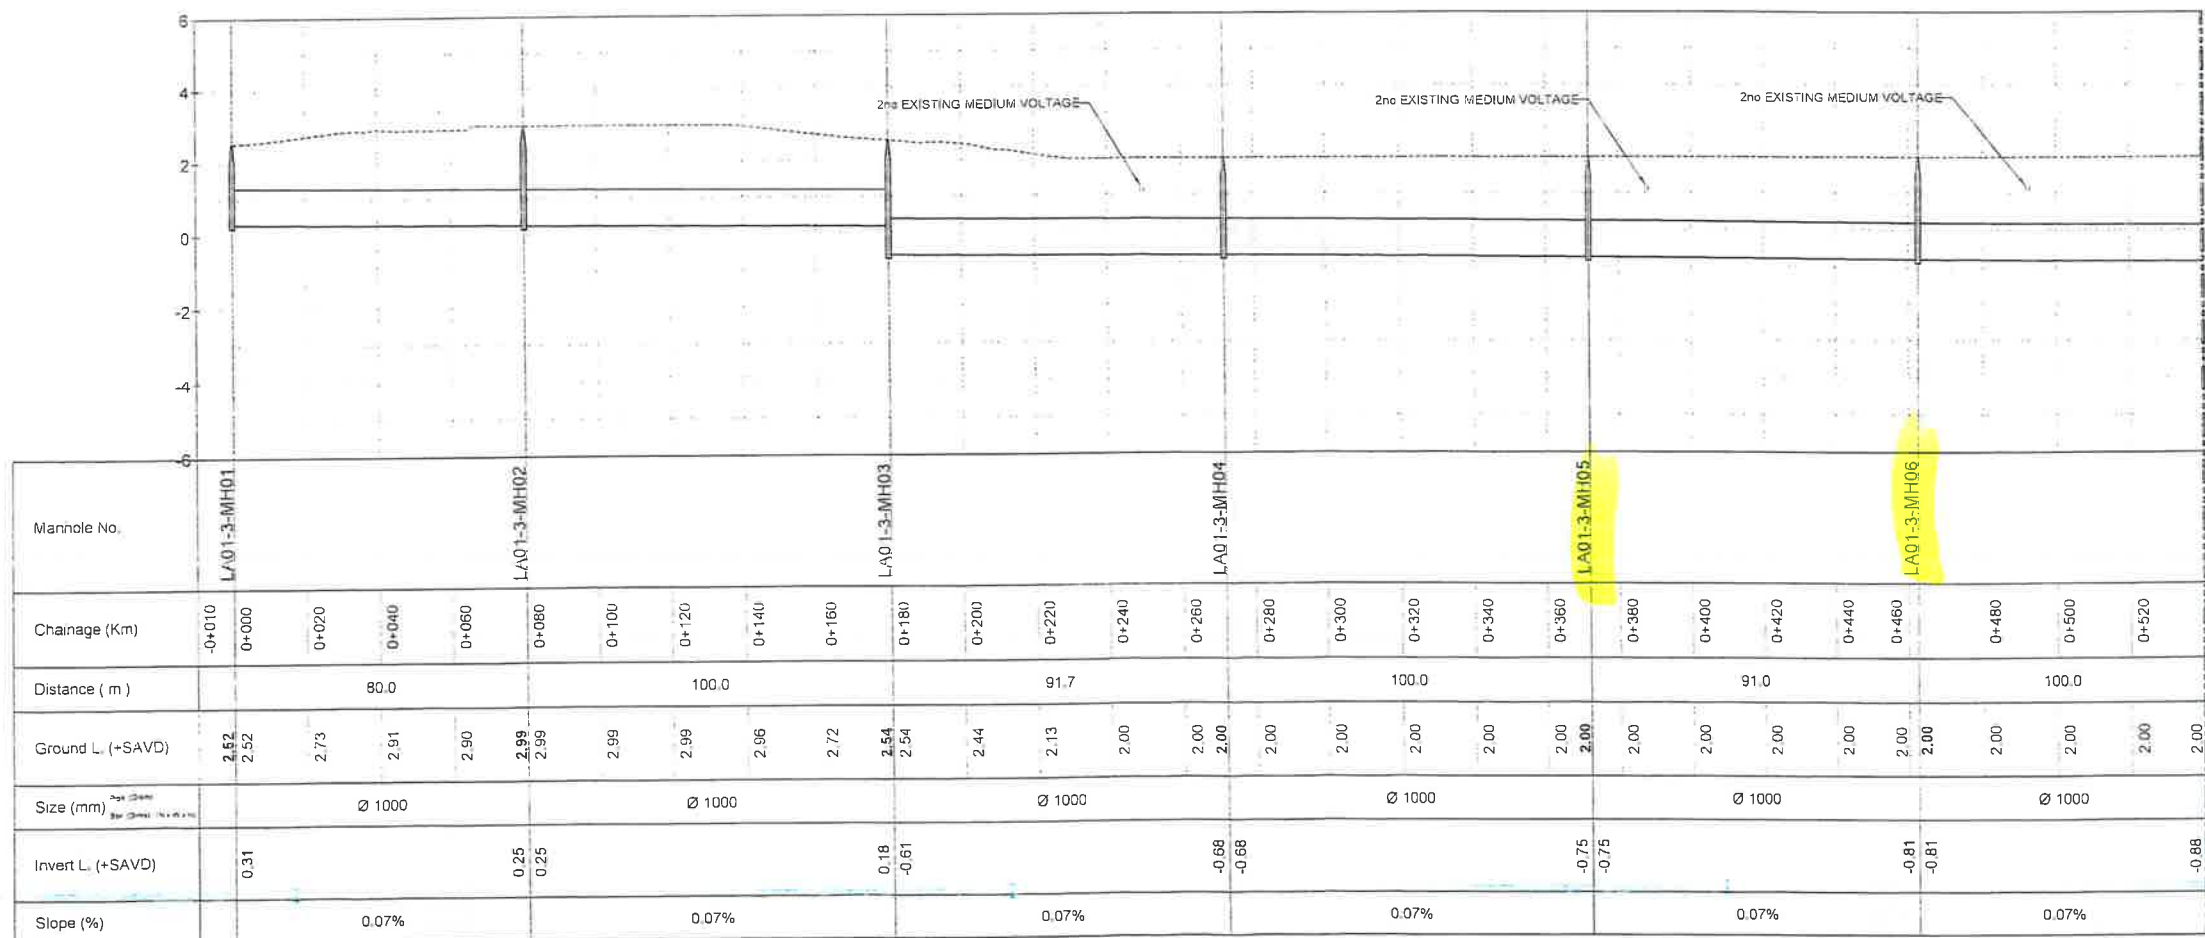

PROFILE L01-3

SCALE: H 1:1000 V 1:10



CONTINUATION - REFER TO JSWM-ACM-XXXX-SW-DR-CE-01211

CONTINUATION - REFER TO JSWM-ACM-XXXX-SW-DR-CE-01218

AECOM

PROJECT

JEDDAH
STORMWATER
AND MASTERPLAN

CLIENT

**Jeddah
Municipality**

CONSULTANT

AECOM Arabia Ltd. Co.
P.O. Box 50000, Jeddah, Saudi Arabia
Al Rawdan Street, P.O. Box 15382
Jeddah 21444, Saudi Arabia
T: +966 12 606 9170 F: +966 12 606 9225
www.aecom.com

NOTES

1. FOR ABBREVIATIONS AND LEGEND REFER TO DRAWING NO. JSWM-ACM-XXXX-SW-DR-CE-01211
2. FOR GENERAL NOTES REFER TO DRAWING NO. JSWM-ACM-XXXX-SW-DR-CE-01212
3. LOCATIONS OF PROPOSED PROTECTION BASINS ARE INDICATIVE ONLY. CONTRACTOR SHALL DETERMINE AND VERIFY THE SETTINGS TO ENSURE CORRECT INSTALLATION AT LOW POINTS.
4. FOR MANHOLE/PRODS & CATCH BASINS DETAIL REFER TO STANDARD DRAWINGS.
5. FOR MANHOLE/PRODS SCHEDULE REFER TO DRAWING NO. JSWM-ACM-XXXX-SW-DR-CE-06201 TO CE-06205.
6. THE CONTRACTOR SHOULD VERIFY/PROVIDE ALL REQUIRED EXISTING UTILITIES INVERT LEVELS/DATA BEFORE THE EXECUTION.
7. THE UTILITIES SHOWN ARE BASED ON INFORMATION OBTAINED FROM AMANAH GIS UTILITY DATABASE DESCRIBED IN THE SCOPE OF WORKS DOCUMENTS. IT IS THE CONTRACTOR'S RESPONSIBILITY TO PROVE THE UTILITIES BEFORE STARTING THE WORK AND REPORT ANY DISCREPANCIES.
8. THE CONTRACTOR SHOULD VERIFY GROUND LEVELS AND SUBMIT DETAILED SHOP DRAWINGS BASED ON ACTUAL SITE SURVEY BEFORE STARTING EXCAVATION FOR PIPE LAYING.

KEY PLAN



ISSUE/REVISION

NO.	DATE	DESCRIPTION
001	26-MAR-2021	STAGE 3 - DETAIL DESIGN & TENDER DOCUMENTS

PURPOSE OF ISSUE

STAGE 3 - DETAIL DESIGN & TENDER DOCUMENTS

PROJECT NUMBER

60555960

SHEET TITLE

DRAINAGE SOLUTION FOR
AL SAWARI AREA
PLAN & PROFILE - LINE LA01-3
SHEET (1 OF 3)

SHEET NUMBER

JSWM-ACM-XXXX-SW-DR-CE-01217
