

WORK INSPECTION REQUEST (WIR) - طلب فحص الأعمال

(Work Inspection Requests should be submitted at least 24 hours prior to inspection time)

WIR No. JSW-YC-SWRI-WIR-SU-0748

Rev. No.: 0

PROJECT - أسم المشروع	CONTRACT - العقد	OWNER - المالك	CONTRACTOR - المقاول
Jeddah Stormwater Drainage (JSWD)	Drainage Solution For Al Sawari Area & King Saud PS	Jeddah Municipality	AL-YAMAMA CO.

Consultant : WSP

Previous Activity WIR No:

ITP Item No:

Work Description (وصف الأعمال)

Excavation for Pipeline from Manhole (MH05 - MH06), Line (LA01-3), Dia-1000 mm, RC Pipe From Station (0 TO 90.37)

B.O.Q: B1 (1.1.1)

Location (المكان): LA01-3

Compliance Statement: The Contractor hereby confirms that The Works offered for inspections are ready and complies with Contract documents & are internally inspected by contractor QC Engineer (in case of mandatory stop point inspection in the ITP, the contractor shall not proceed without approval)

Drawing Ref. No. JSWM-ACM-AXXX-SW-DR-CE-01217

Inspection Date: 18/05/2025

Inspection Time: 9:00 am

DISCIPLINE - التخصص

- ☐ Local Drainage ☐ Hydraulics
☐ Roads ☐ Geotechnical
☐ Micro-Tunnelling ☒ Civil / Structural
☐ Utilities ☐ Architectural

- ☐ Mechanical
☐ Electrical
☐ HSE

☐ Other (specify):

Requested by:

Engr. Elhabib Musa
Contractor QC Representative
ممثل مراقبة الجودة للمقاول

Signature
التوقيع

Date
التاريخ

WSP Inspector Remarks (ملاحظات المشرف):

checked

WSP Engineer Remarks (ملاحظات المهندس):

INSPECTION RESULT - نتيجة الفحص

The Works are: ☒ A: Approved
يعتمد

☐ B: Approved with Comments -
يعتمد مع ملاحظات - يعاد تقديمه
Resubmit

☐ C: Not Approved -
مرفوض

☐ D: Rejected

WSP Inspector:

Name: Eslam adel
Signature: Eslam
Date: 24/06/2025

WSP Engineer:

Name: Rashid Habash
Signature: Rashid
Date: 25.06.2025

Contractor:

Received:
Signature:
Date:

Note: The Engineer's / Consultants approval shall not in any way relieve The Contractor of his obligation under The Contract. The Contractor shall be solely responsible for The correctness, quality and coordination of The Works being offered for inspection as per The applicable Contract Conditions and Contract Clauses. Consultants' comments on The inspection requests shall not be construed as instruction to vary The scope of Contractor by whatsoever means

SHEET FOR EARTH EXCAVATION DETAILS AND TOP OF PIPE

NAME OF STREET:	Existing Asphalt = 0.12m	W. Asph. =	2.504	MH SIZE	MH05(2400*2400)	MH 06(2400*2400)
LINE NO:	LA01-3	SHEET NO.:	Existing ABC = 0.30M	MH WALL THICKNESS	350mm	350mm
SLOPE:	0.067%	FROM STA:	TO STA:	MH BASE THICKNESS	350mm	
WIDTH:	2.504	DIAMETER & KIND OF PIPE:	1000mm	MH BASE LEVEL	-1.100	-1.161
THICKNESS:	0.127	BEDDING:	0.15	Depth to MH BASE	3.019	3.036
			LENGTH :C.C		90.37	
			NET LENGTH:		87.27	

M.H. NO.	S.T	DISTANCE	GROUND LEVEL	TYPE OF LINE RC&UPVC	INVERT LEVEL	EXCAVATION LEVEL	TOP OF PIPE LEVEL	ACTUAL TOP OF PIPE	ACTUAL EXCAVATION LEVEL	DIFFERENCE	rock.L	REMARKS
MH05	0	0.000	1.919	Parallel	-0.750	-1.825						509548.058
-	1.20	1.200	1.919	Parallel	-0.751	-1.028	0.376					2410744.114
-	1.55	0.350	1.919	Parallel	-0.751	-1.028	0.376					
sp	2.67	1.120	1.919	Parallel	-0.752	-1.029	0.375					
1	5.17	2.500	1.919	Parallel	-0.753	-1.030	0.374					
2	7.67	2.500	1.919	Parallel	-0.755	-1.032	0.372					
3	10.17	2.500	1.919	Parallel	-0.757	-1.034	0.370					
4	12.67	2.500	1.919	Parallel	-0.758	-1.035	0.369					
5	15.17	2.500	1.919	Parallel	-0.760	-1.037	0.367					
6	17.67	2.500	1.919	Parallel	-0.762	-1.039	0.365					
7	20.17	2.500	1.920	Parallel	-0.764	-1.041	0.363					
8	22.67	2.500	1.920	Parallel	-0.765	-1.042	0.362					
9	25.17	2.500	1.900	Parallel	-0.767	-1.044	0.360					
10	27.67	2.500	1.900	Parallel	-0.769	-1.046	0.358					
11	30.17	2.500	1.900	Parallel	-0.770	-1.047	0.357					
12	32.67	2.500	1.900	Parallel	-0.772	-1.049	0.355					
13	35.17	2.500	1.900	Parallel	-0.774	-1.051	0.353					
14	37.67	2.500	1.900	Parallel	-0.775	-1.052	0.352					
15	40.17	2.500	1.900	Parallel	-0.777	-1.054	0.350					
16	42.67	2.500	1.900	Parallel	-0.779	-1.056	0.348					
17	45.17	2.500	1.900	Parallel	-0.780	-1.057	0.347					
18	47.67	2.500	1.900	Parallel	-0.782	-1.059	0.345					
19	50.17	2.500	1.900	Parallel	-0.784	-1.061	0.343					
20	52.67	2.500	1.900	Parallel	-0.785	-1.062	0.342					
21	55.17	2.500	1.900	Parallel	-0.787	-1.064	0.340					
22	57.67	2.500	1.900	Parallel	-0.789	-1.066	0.338					
23	60.17	2.500	1.900	Parallel	-0.790	-1.067	0.337					
24	62.67	2.500	1.900	Parallel	-0.792	-1.069	0.335					
25	65.17	2.500	1.900	Parallel	-0.794	-1.071	0.333					
26	67.67	2.500	1.900	Parallel	-0.795	-1.072	0.332					
27	70.17	2.500	1.900	Parallel	-0.797	-1.074	0.330					
28	72.67	2.500	1.900	Parallel	-0.799	-1.076	0.328					
29	75.17	2.500	1.900	Parallel	-0.800	-1.077	0.327					
30	77.67	2.500	1.900	Parallel	-0.802	-1.079	0.325					
31	80.17	2.500	1.900	Parallel	-0.804	-1.081	0.323					
32	82.67	2.500	1.900	Parallel	-0.805	-1.082	0.322					
33	85.17	2.500	1.900	Parallel	-0.807	-1.084	0.320					
34	87.67	2.500	1.880	Parallel	-0.809	-1.086	0.318					
SP	88.82	1.150	1.880	Parallel	-0.810	-1.087	0.317					
-	89.17	0.350	1.875	Parallel	-0.810	-1.087	0.317					509517.384
MH06	90.37	1.200	1.875	Parallel	-0.811	-1.886						2410829.119

CONTRACTOR

CONSULTANT

SURVEYOR

PROJECT MANAGER

SURVEYOR

RESIDENT ENGINEER

LEGEND

- PROPOSED MANHOLE
- DIRECTION OF FLOW
- PROPOSED DRAINAGE PIPE
- PROPOSED PROTECTIVE BASIN
- EXISTING STRUCTURE
- EXISTING WATER
- EXISTING WASTE
- EXISTING POWER
- EXISTING TELECOM
- PROPOSED CHANNEL
- PROPOSED TUNNEL
- PROPOSED SHAFT
- PROPOSED INTERCEPTION
- PROPOSED OUTFALL



NOTES

1. ALL DIMENSIONS ARE IN METERS UNLESS OTHERWISE NOTED

LA01-3-MH5\RC
X=509548.058
Y=2410744.114
GL=1.919
IL=-0.750
Depth=2.669

Dim=Ø400

L=90.37 m
Dim=Ø1000

LA01-3-MH5\UPVC
GL=1.919
IL=-0.150
Depth=2.069

LA01-3-MH6\RC
X=509517.384
Y=2410829.119
GL=1.875
IL=-0.811
Depth=2.686

LA01-3-MH6\UPVC
GL=1.875
IL=-0.211
Depth=2.086



ساحل بلخايط

ساحل بلخايط

جدة أمية

OWNER

CAPS A04

MANAGER

DESIGNER

CONSULTANT

STAMP

WSP

APPROVAL

DATE

SIGNATURE

APPROVED WITH COMMENTS

REMARKS

NOT APPROVED - REWORK

SELECTED

STAMP

DATE

SIGNATURE

APPROVED WITH COMMENTS

REMARKS

NOT APPROVED - REWORK

SELECTED

STAMP

DATE

SIGNATURE

APPROVED WITH COMMENTS

REMARKS

NOT APPROVED - REWORK

SELECTED

STAMP

DATE

SIGNATURE

APPROVED WITH COMMENTS

REMARKS

NOT APPROVED - REWORK

SELECTED

STAMP

GENERAL LAYOUT OVER ALL PLAN

PROJECT NUMBER: 001.75131.04.00.04

DRAWN BY: ARCH

CHECKED BY: CIVIL/ARCH

TITLE: MECH

SUBMITTAL NO.

DRAWING NUMBER

REV. NO.


SCALE

SHEET NO.

T OF 1


1. 2. 3. 4. 5. 6. 7. 8. 9. 10. 11. 12. 13. 14. 15. 16. 17. 18. 19. 20. 21. 22. 23. 24. 25. 26. 27. 28. 29. 30. 31. 32. 33. 34. 35. 36. 37. 38. 39. 40. 41. 42. 43. 44. 45. 46. 47. 48. 49. 50. 51. 52. 53. 54. 55. 56. 57. 58. 59. 60. 61. 62. 63. 64. 65. 66. 67. 68. 69. 70. 71. 72. 73. 74. 75. 76. 77. 78. 79. 80. 81. 82. 83. 84. 85. 86. 87. 88. 89. 90. 91. 92. 93. 94. 95. 96. 97. 98. 99. 100. 101. 102. 103. 104. 105. 106. 107. 108. 109. 110. 111. 112. 113. 114. 115. 116. 117. 118. 119. 120. 121. 122. 123. 124. 125. 126. 127. 128. 129. 130. 131. 132. 133. 134. 135. 136. 137. 138. 139. 140. 141. 142. 143. 144. 145. 146. 147. 148. 149. 150. 151. 152. 153. 154. 155. 156. 157. 158. 159. 160. 161. 162. 163. 164. 165. 166. 167. 168. 169. 170. 171. 172. 173. 174. 175. 176. 177. 178. 179. 180. 181. 182. 183. 184. 185. 186. 187. 188. 189. 190. 191. 192. 193. 194. 195. 196. 197. 198. 199. 200. 201. 202. 203. 204. 205. 206. 207. 208. 209. 210. 211. 212. 213. 214. 215. 216. 217. 218. 219. 220. 221. 222. 223. 224. 225. 226. 227. 228. 229. 230. 231. 232. 233. 234. 235. 236. 237. 238. 239. 240. 241. 242. 243. 244. 245. 246. 247. 248. 249. 250. 251. 252. 253. 254. 255. 256. 257. 258. 259. 260. 261. 262. 263. 264. 265. 266. 267. 268. 269. 270. 271. 272. 273. 274. 275. 276. 277. 278. 279. 280. 281. 282. 283. 284. 285. 286. 287. 288. 289. 290. 291. 292. 293. 294. 295. 296. 297. 298. 299. 300. 301. 302. 303. 304. 305. 306. 307. 308. 309. 310. 311. 312. 313. 314. 315. 316. 317. 318. 319. 320. 321. 322. 323. 324. 325. 326. 327. 328. 329. 330. 331. 332. 333. 334. 335. 336. 337. 338. 339. 340. 341. 342. 343. 344. 345. 346. 347. 348. 349. 350. 351. 352. 353. 354. 355. 356. 357. 358. 359. 360. 361. 362. 363. 364. 365. 366. 367. 368. 369. 370. 371. 372. 373. 374. 375. 376. 377. 378. 379. 380. 381. 382. 383. 384. 385. 386. 387. 388. 389. 390. 391. 392. 393. 394. 395. 396. 397. 398. 399. 400. 401. 402. 403. 404. 405. 406. 407. 408. 409. 410. 411. 412. 413. 414. 415. 416. 417. 418. 419. 420. 421. 422. 423. 424. 425. 426. 427. 428. 429. 430. 431. 432. 433. 434. 435. 436. 437. 438. 439. 440. 441. 442. 443. 444. 445. 446. 447. 448. 449. 450. 451. 452. 453. 454. 455. 456. 457. 458. 459. 460. 461. 462. 463. 464. 465. 466. 467. 468. 469. 470. 471. 472. 473. 474. 475. 476. 477. 478. 479. 480. 481. 482. 483. 484. 485. 486. 487. 488. 489. 490. 491. 492. 493. 494. 495. 496. 497. 498. 499. 500. 501. 502. 503. 504. 505. 506. 507. 508. 509. 510. 511. 512. 513. 514. 515. 516. 517. 518. 519. 520. 521. 522. 523. 524. 525. 526. 527. 528. 529. 530. 531. 532. 533. 534. 535. 536. 537. 538. 539. 540. 541. 542. 543. 544. 545. 546. 547. 548. 549. 550. 551. 552. 553. 554. 555. 556. 557. 558. 559. 560. 561. 562. 563. 564. 565. 566. 567. 568. 569. 570. 571. 572. 573. 574. 575. 576. 577. 578. 579. 580. 581. 582. 583. 584. 585. 586. 587. 588. 589. 590. 591. 592. 593. 594. 595. 596. 597. 598. 599. 600. 601. 602. 603. 604. 605. 606. 607. 608. 609. 610. 611. 612. 613. 614. 615. 616. 617. 618. 619. 620. 621. 622. 623. 624. 625. 626. 627. 628. 629. 630. 631. 632. 633. 634. 635. 636. 637. 638. 639. 640. 641. 642. 643. 644. 645. 646. 647. 648. 649. 650. 651. 652. 653. 654. 655. 656. 657. 658. 659. 660. 661. 662. 663. 664. 665. 666. 667. 668. 669. 670. 671. 672. 673. 674. 675. 676. 677. 678. 679. 680. 681. 682. 683. 684. 685. 686. 687. 688. 689. 690. 691. 692. 693. 694. 695. 696. 697. 698. 699. 700. 701. 702. 703. 704. 705. 706. 707. 708. 709. 710. 711. 712. 713. 714. 715. 716. 717. 718. 719. 720. 721. 722. 723. 724. 725. 726. 727. 728. 729. 730. 731. 732. 733. 734. 735. 736. 737. 738. 739. 740. 741. 742. 743. 744. 745. 746. 747. 748. 749. 750. 751. 752. 753. 754. 755. 756. 757. 758. 759. 760. 761. 762. 763. 764. 765. 766. 767. 768. 769. 770. 771. 772. 773. 774. 775. 776. 777. 778. 779. 780. 781. 782. 783. 784. 785. 786. 787. 788. 789. 790. 791. 792. 793. 794. 795. 796. 797. 798. 799. 800. 801. 802. 803. 804. 805. 806. 807. 808. 809. 810. 811. 812. 813. 814. 815. 816. 817. 818. 819. 820. 821. 822. 823. 824. 825. 826. 827. 828. 829. 830. 831. 832. 833. 834. 835. 836. 837. 838. 839. 840. 84

CONTRACTOR SIGNATURE

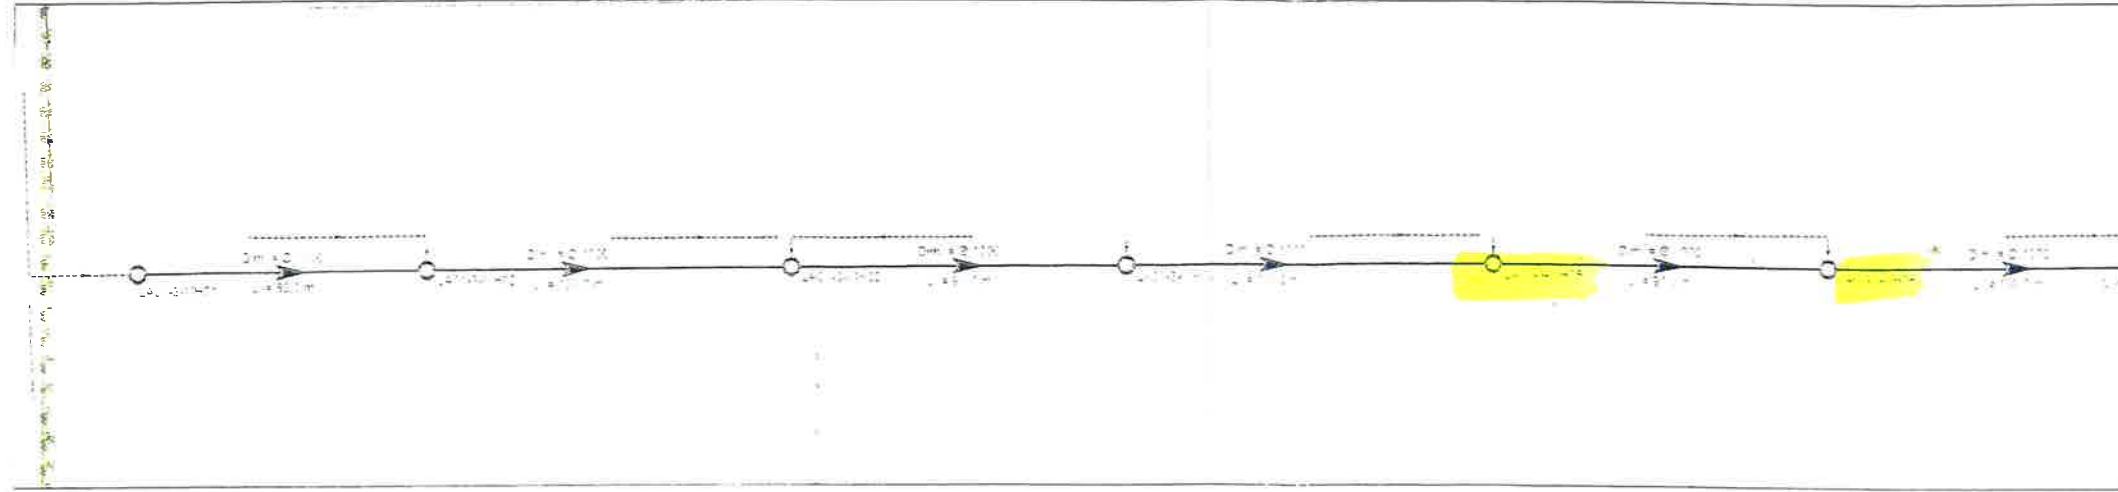

PLAN L01-3

Scale: H 1:1000

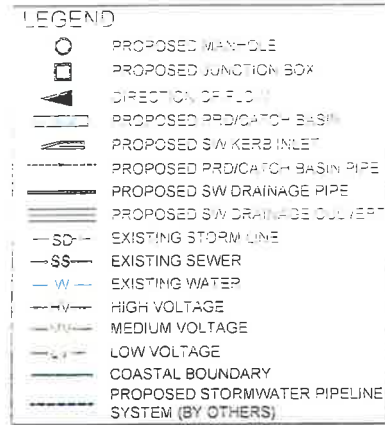

NOTES

- CONTRACTOR MUST CONFIRM EXISTING UTILITIES TYPE, SIZE, LOCATION AND DEPTH ALONG PIPELINE ROUTE PRIOR TO COMMENCING WORKS. SOME UTILITIES SUCH AS STC AND MOBIILITY ARE OMITTED FOR CLARITY. REFER TO DRAWINGS JSWM-ACM-AXX-UT-OR-CE-01201 - 01233.
- STAKEHOLDERS MUST BE CONSULTED WITH REGARD TO THE PIPELINE ROUTE.
- A GEOPHYSICAL SURVEY SHOULD BE CARRIED OUT PRIOR TO WORKS COMMENCING.
- PIPES WITH INSUFFICIENT COVER TO BE CONCRETE ENCASED. REFER TO STANDARD DETAILS.
- RELOCATE UTILITY BASED ON SITE CONDITIONS.



AECOM

PROJECT

JEDDAH
STORMWATER
AND MASTERPLAN

CLIENT



CONSULTANT

AECOM Arabia Ltd. Co.
P.O. Box 51, Jeddah, Saudi Arabia
Al Rawdan Street, P.O. Box 15362
Jeddah 21444, Saudi Arabia
T: +966 12 606 9170 F: +966 12 606 9205
www.aecom.com

NOTES

- FOR ABBREVIATIONS AND LEGEND REFER TO DRAWING NO. JSWM-ACM-AXX-UT-OR-CE-00200.
- FOR GENERAL NOTES REFER TO DRAWING NO. JSWM-ACM-AXX-XX-DR-ZZ-00204.
- LOCATIONS OF PROPOSED PRO/CATCH BASINS ARE INDICATIVE ONLY. CONTRACTOR SHALL DETERMINE AND VERIFY THE SETTINGS TO ENSURE CORRECT INSTALLATION AT LOW POINTS.
- FOR MANHOLE/PRO/CATCH BASIN SCHEDULES REFER TO STANDARD DRAWINGS.
- FOR MANHOLE/PRO/CATCH SCHEDULES REFER TO DRAWING NO. JSWM-ACM-AXX-SW-OR-CE-06201 TO CE-06205.
- THE CONTRACTOR SHOULD VERIFY/PROVIDE ALL REQUIRED EXISTING UTILITIES INVERT LEVELS/DATA BEFORE THE EXECUTION.
- THE UTILITIES SHOWN ARE BASED ON INFORMATION OBTAINED FROM AMANAH GIS UTILITY DATABASE DESCRIBED IN THE SCOPE OF WORKS DOCUMENTS. IT IS THE CONTRACTOR'S RESPONSIBILITY TO PROVE THE UTILITIES BEFORE STARTING THE WORK AND REPORT ANY DISCREPANCIES.
- THE CONTRACTOR SHOULD VERIFY GROUND LEVELS AND SUBMIT DETAILED SHOP DRAWINGS BASED ON ACTUAL SITE SURVEY BEFORE STARTING EXCAVATION FOR PIPE LAYING.

KEY PLAN



ISSUE/REVISION

| NO. | DATE | DESCRIPTION |
|-----|-------------|--|
| C01 | 26-MAR-2021 | STAGE 3 - DETAIL DESIGN & TENDER DOCUMENTS |

PURPOSE OF ISSUE

STAGE 3 - DETAIL DESIGN & TENDER DOCUMENTS

PROJECT NUMBER


60555960

SHEET TITLE

DRAINAGE SOLUTION FOR
AL SAWARI AREA
PLAN & PROFILE - LINE LA01-3
SHEET (1 OF 3)

SHEET NUMBER

JSWM-ACM-AXX-SW-DR-CE-01217

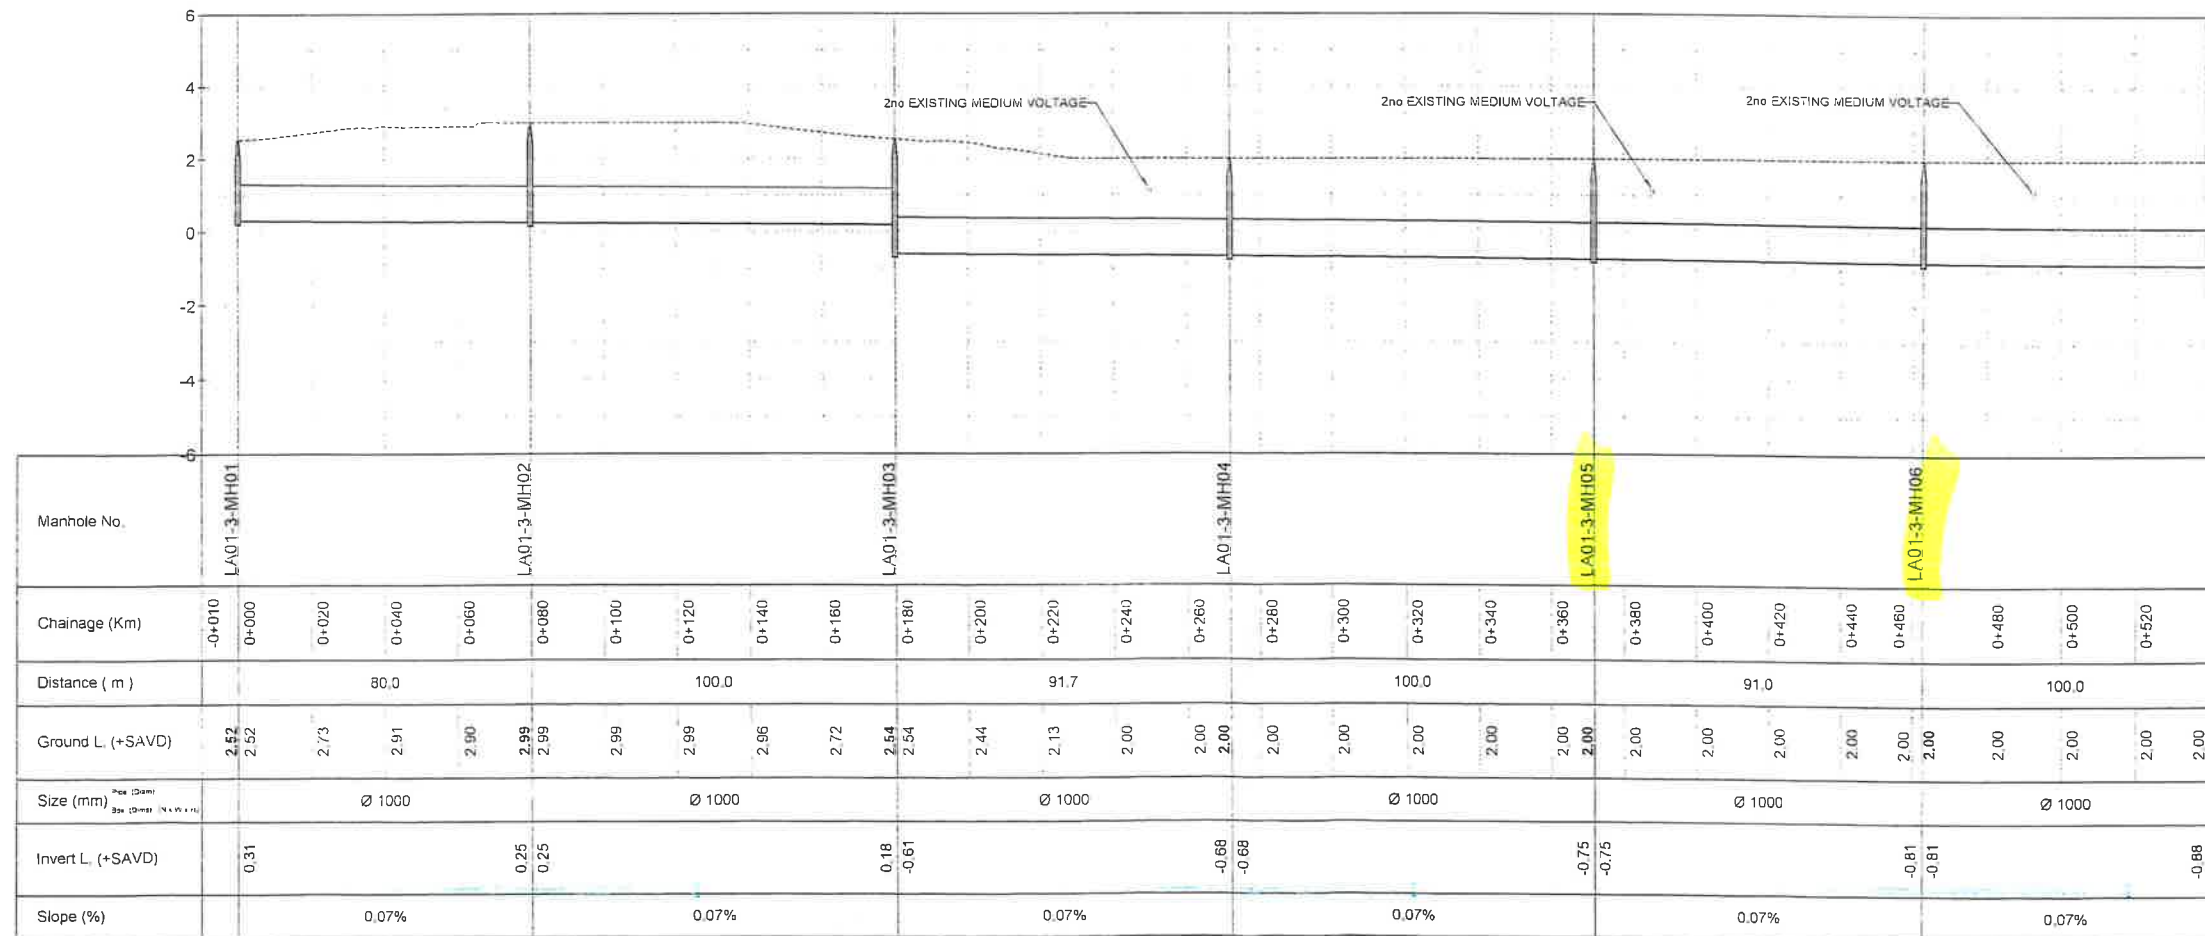

PROFILE L01-3

SCALE: H 1:1000 V 1:10

CONTINUATION - REFER TO JSWM-ACM-AXX-SW-DR-CE-01218
